


IPGPL 14 RTGs Iran



No	Task	Duration	Start	Finish	2019																
					1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
1	Preliminary Project Schedule	455 days	2018-04-06	2019-07-05																	
2	LC opening	0 days	2018-04-06	2018-04-06																	
3	Engineering	45 days	2018-04-06	2018-05-21																	
4	Long lead time release	14 days	2018-04-06	2018-04-20																	
5	Design review	35 days	2018-04-06	2018-05-11																	
6	Design approved and frozen	2 days	2018-05-11	2018-05-13																	
7	Other components list release	8 days	2018-05-13	2018-05-21																	
8	Purchasing	136 days	2018-04-20	2018-09-03																	
9	Long lead time items	135 days	2018-04-20	2018-09-02																	
10	Component list items	105 days	2018-05-21	2018-09-03																	
11	Production	110 days	2018-04-20	2018-08-08																	
12	Steel structure fabrication	110 days	2018-04-20	2018-08-08																	
13	Factory assembly	90 days	2018-09-03	2018-12-02																	
14	Assembly 1st batch of 7RTGs	45 days	2018-09-03	2018-10-18																	
15	Assembly 2nd batch of 7RTGs	45 days	2018-10-18	2018-12-02																	
16	Final Assembly	90 days	2018-10-18	2019-01-16																	
17	Final assembly 1st batch of 7RTGs	45 days	2018-10-18	2018-12-02																	
18	Final assembly 2nd batch of 7RTGs	45 days	2018-12-02	2019-01-16																	
19	Commissioning & testing	105 days	2018-11-12	2019-02-25																	
20	Commissioning & testing 1st batch of 7RTGs	60 days	2018-11-12	2019-01-11																	
21	Commissioning & testing 2nd batch of 7RTGs	60 days	2018-12-27	2019-02-25																	
22	Shipment	82 days	2019-01-11	2019-04-03																	
23	Loading 1st batch of 7RTGs	4 days	2019-01-11	2019-01-15																	
24	Sea transportation	22 days	2019-01-15	2019-02-06																	
25	Unloading	4 days	2019-02-06	2019-02-10																	
26	Customes clearance	7 days	2019-02-10	2019-02-17																	
27	Loading 2nd batch of 7RTGs	4 days	2019-02-25	2019-03-01																	
28	Sea transportation	22 days	2019-03-01	2019-03-23																	
29	Unloading	4 days	2019-03-23	2019-03-27																	
30	Customes clearance	7 days	2019-03-27	2019-04-03																	
31	Final Commissioning & testing of the 1st 7RTG	46 days	2019-02-17	2019-04-04																	
32	Final Commissioning & testing	45 days	2019-02-17	2019-04-03																	
33	Punchlist	7 days	2019-03-28	2019-04-04																	
34	Handover	0 days	2019-04-04	2019-04-04																	
35	Final Commissioning & testing of the 2nd 7RTG	70 days	2019-04-04	2019-06-13																	
36	Final Commissioning & testing	45 days	2019-04-04	2019-05-19																	
37	Punchlist	14 days	2019-05-30	2019-06-13																	
38	Handover	0 days	2019-06-13	2019-06-13																	

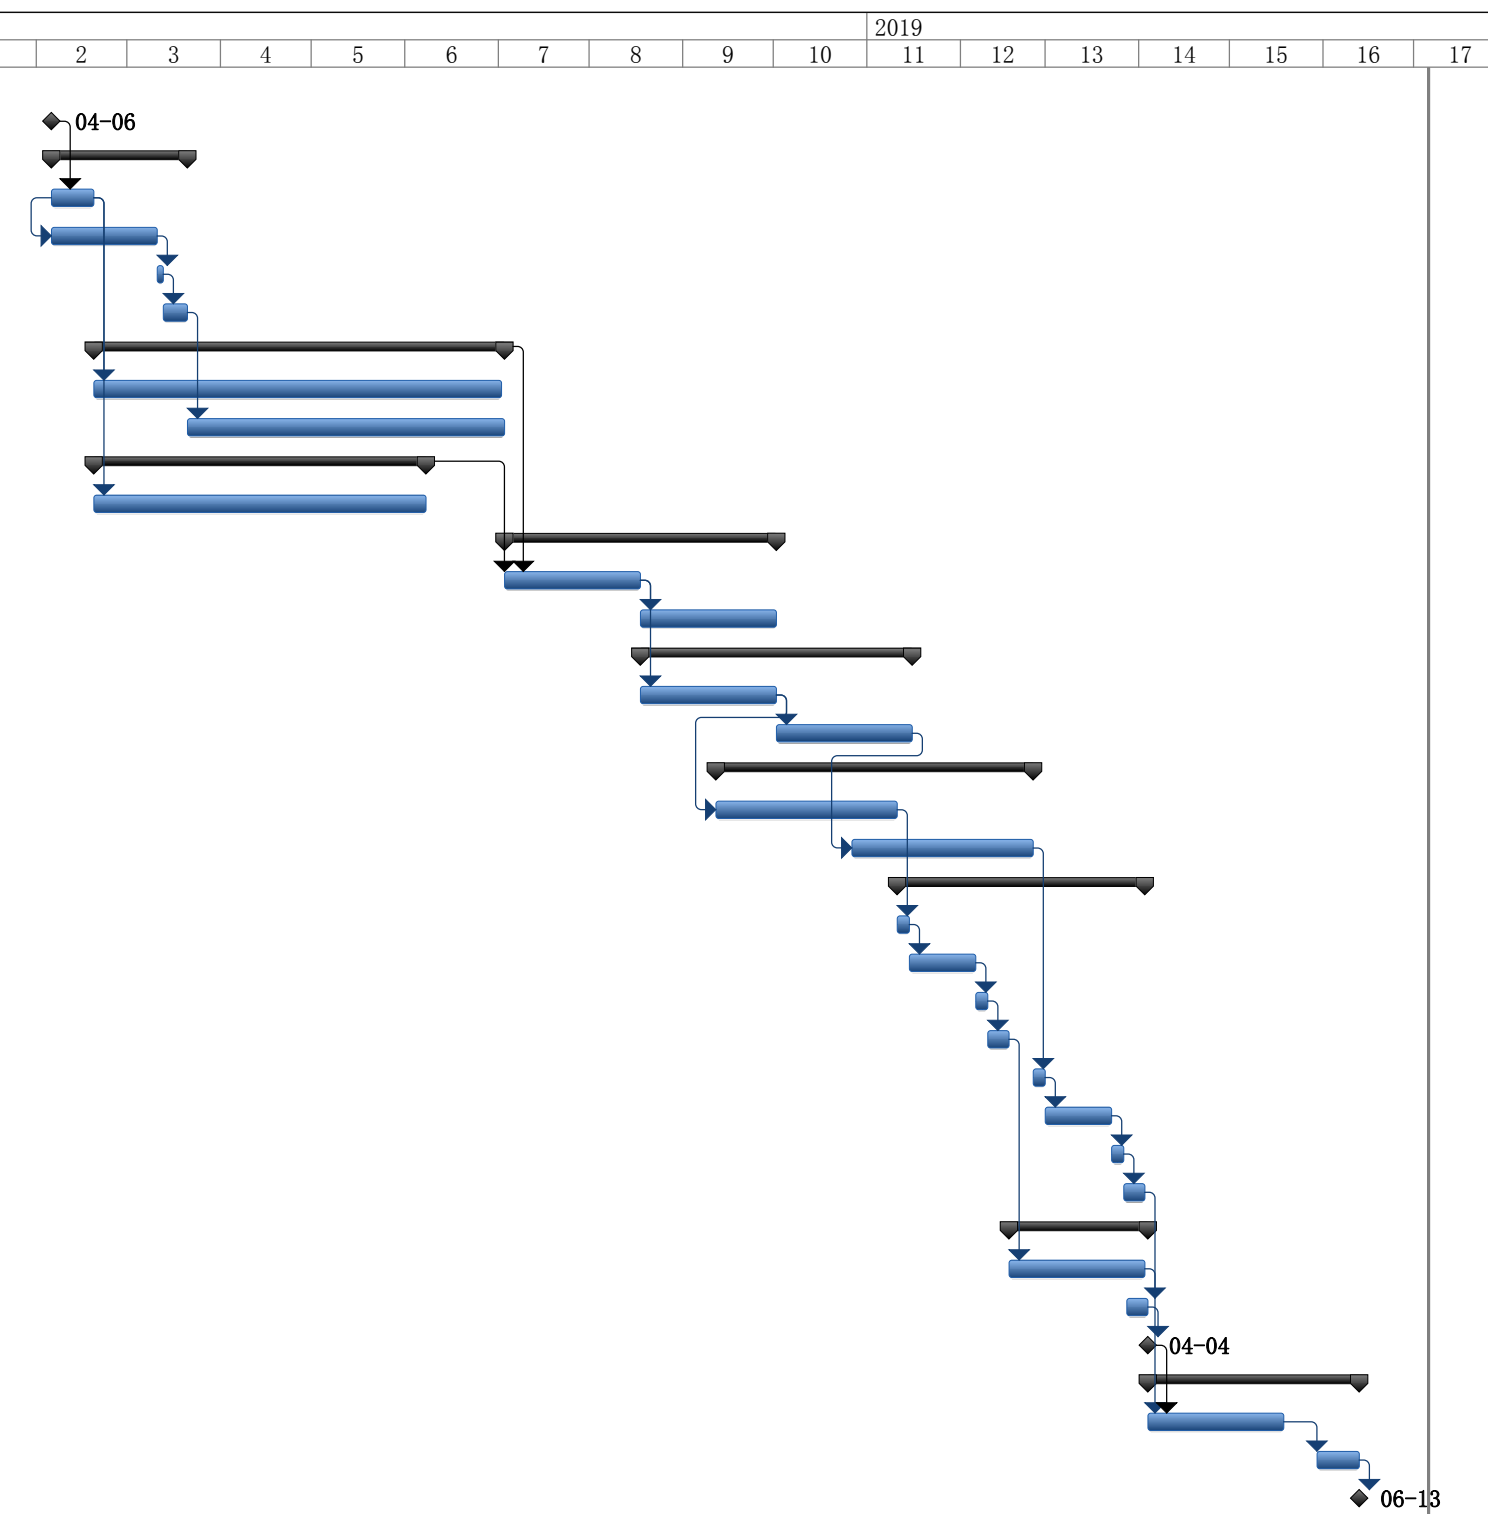

Project: IPGPL 14RTGs Iran
Date: 2018-03-15

Task Splik Milepost Summary Project Summary Progress
